Strudcom consultants Observation point complince Tower-9 8th slab Pour-1

Checking Date : 04/10/2025 | Closing Date : 04/10/2025

Observation Report

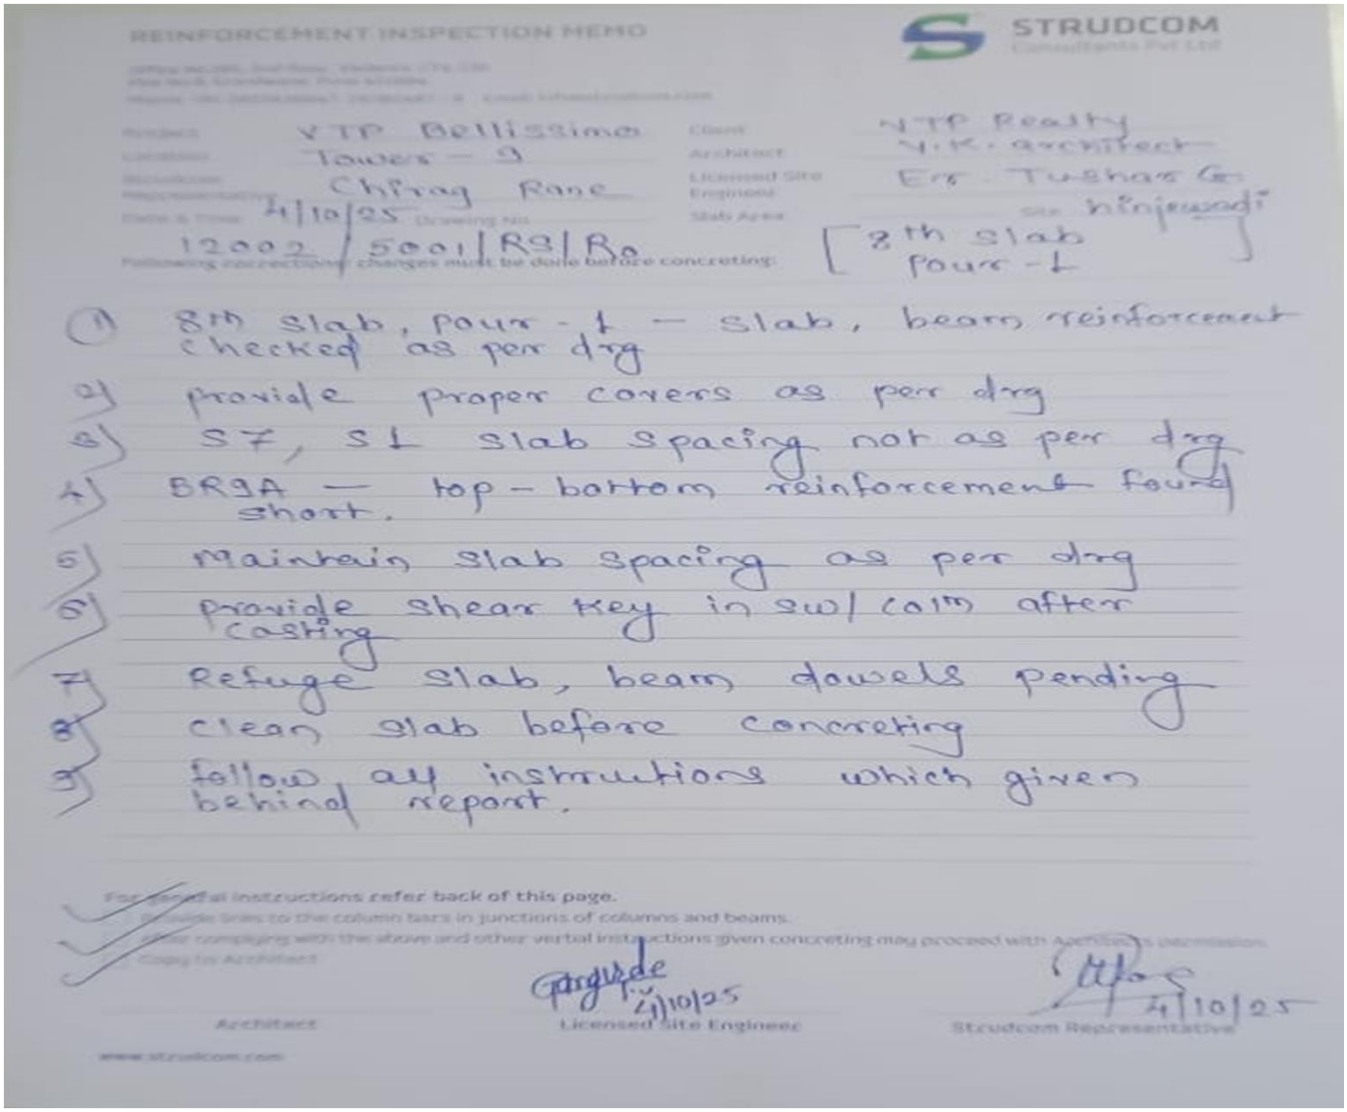

REINFORCEMENT INSPECTION MEMO

STRUDCOM

Project: VTP Bellissimo Tower – 9
Client: VTP Realty
Architect: Y.K. architect
Licensed Site Engineer: Er. Tushar G. Chirag Rane
Date & Time: 4/10/25
Slab Area: 8th slab pour-1
Drawing No: 12002/5001/R9/R0

Following corrections/changes must be done before concreting:

1) 8th slab, pour-1 – slab, beam reinforcement checked as per drg
2) provide proper covers as per drg
3) S7, S1 slab spacing not as per drg
4) BR9A – top-bottom reinforcement found short.
5) Maintain slab spacing as per drg
6) provide shear key in sw/ cm after casting
7) Refuge slab, beam dowels pending
8) Clean slab before concreting
9) follow all instructions which given behind report.

For detailed instructions refer back of this page.
Provide ties to the column bars in junctions of columns and beams.
After complying with the above and other verbal instructions given concreting may proceed with Architect's permission.
Copy to Architect

Architect | Licensed Site Engineer 4/10/25 | Strudcom Representative 4/10/25

www.strudcom.com

Sr. No.	Observation	Location	After Rectification Picture
3	S7, S1 Slab Spacing not as per drg.	T-9	

4	BR9A top bottom reinforcement found short.	T-9	
7	Refuge slab, Beam dowels pending.	T-9	
